




**FIRST LAYER OF WASTE:**  
 - 500mm to 1000mm uncompacted  
 - to protect clay liner and leachate collection system

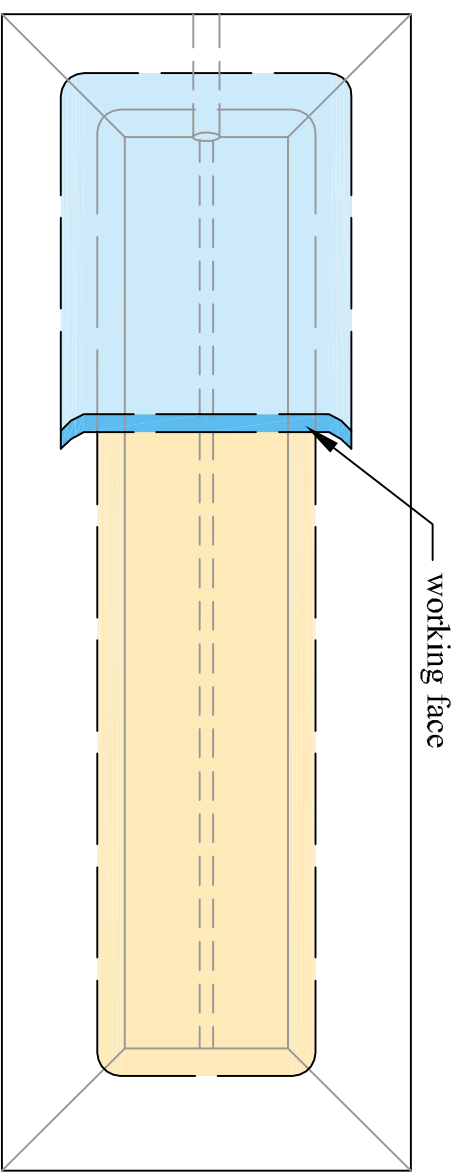


**PROGRESSIVE COMPACTED LIFTS:**  
 - compacted thickness 400mm to 500mm  
 - place and compact from manhole end to high end in each lift

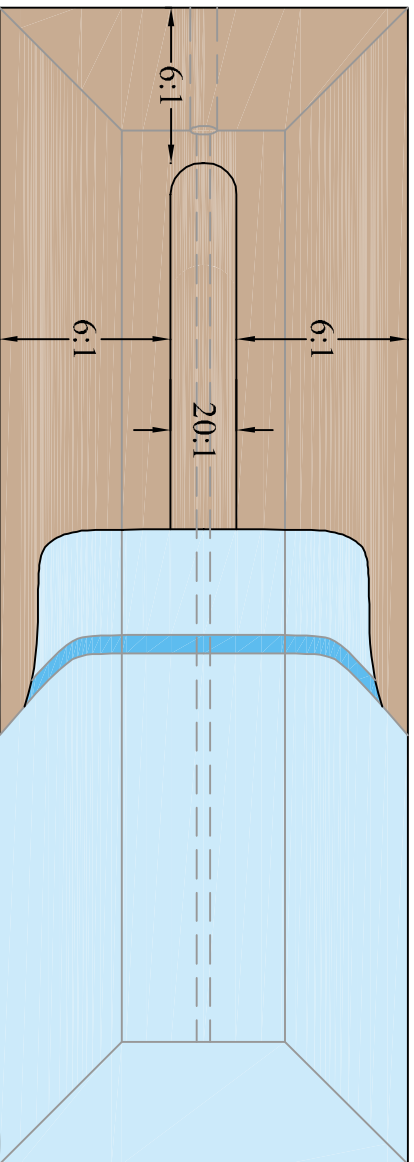

**ABOVE GROUND CONSTRUCTION:**  
 - with progressive final cover

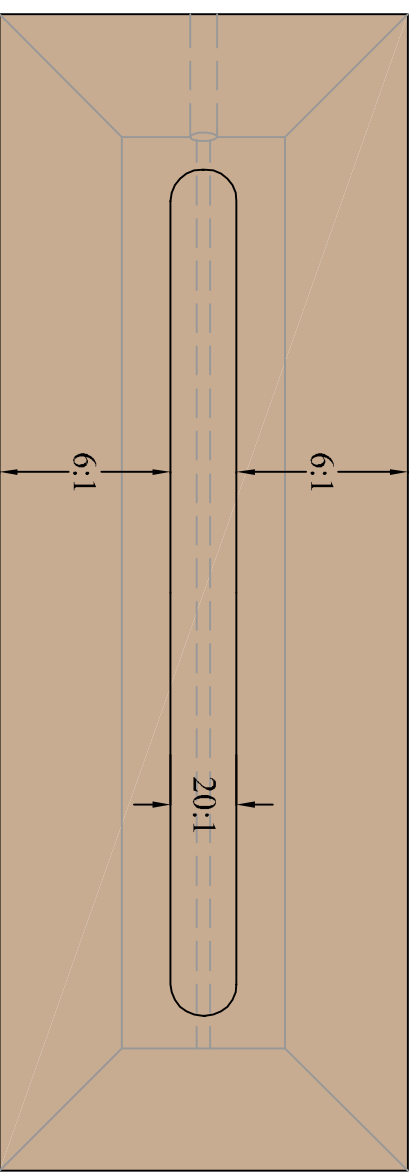

**FINAL COVER COMPLETE**  
 - 1,000mm compacted clay  
 - 300mm topsoil  
 - seed to grass

**LEGEND**  
  
 FIRST WASTE LAYER  
 COMPACTED WASTE AND COVER SOIL  
 FINAL COVER

NO.	DATE	ENG.	BY	SUBJECT

REVISIONS



Madison RS Engineering Inc.



DATE:	28 JUL 15	DRAWN BY:	WMB	APPROVED BY:	WAJ
SCALE:	NTS	WM FILE NO.:	WM372.2	WM FIGURE NO.:	7.4
CLIENT:	REACT	PROJECT:	REGIONAL LANDFILL - DEVELOPMENT PERMIT	TITLE:	LANDFILL CELL - WASTE PLACEMENT
